



ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	2017	2018	2019	2020	2021	2022	2023
0		WRD025-03-02-WSS to Kodassery Pariyaram and Athirappilly Panchayaths in Thrissur District - Package II	1162 days	13-11-18	30-07-22	₹ 162,063,923.08	₹ 162,063,923.08							
1		Project Start	0 days	13-11-18	13-11-18	₹ 0.00	₹ 0.00							
2		Pre-Construction Work	512 days	13-11-18	01-07-20	₹ 0.00	₹ 0.00							
3		TS, Tender Process & Execution of work contract	512 days	13-11-18	01-07-20	₹ 0.00	₹ 0.00							
4		Issuing of Administrative Sanction	1 day	13-11-18	13-11-18	₹ 0.00	₹ 0.00							
5		Issuing of Technical Sanction	1 day	22-11-19	22-11-19	₹ 0.00	₹ 0.00							
6		Publishing of Tender Notice	1 day	28-12-19	28-12-19	₹ 0.00	₹ 0.00							
7		Opening of the technical bid	1 day	03-02-20	03-02-20	₹ 0.00	₹ 0.00							
8		Opening of the financial bid	1 day	10-03-20	10-03-20	₹ 0.00	₹ 0.00							
9		Award of Work	1 day	29-06-20	29-06-20	₹ 0.00	₹ 0.00							
10		Signing of Agreement with Contractor	1 day	30-06-20	30-06-20	₹ 0.00	₹ 0.00							
11		Site Hand over to the contractor	1 day	01-07-20	01-07-20	₹ 0.00	₹ 0.00							
12		Contract Work	624 days	01-07-20	28-06-22	₹ 162,063,923.08	₹ 0.00							
13		Engg. & Design	20 days	01-07-20	23-07-20	₹ 0.00	₹ 0.00							
14		Approval from KWA	20 days	01-07-20	23-07-20	₹ 0.00	₹ 0.00							
15		Gravity Main	17 days	01-07-20	20-07-20	₹ 0.00	₹ 0.00							
16		Submission of QAP to KWA by Contractor	2 days	01-07-20	02-07-20	₹ 0.00	₹ 0.00							
17		QAP approval from KWA	7 days	03-07-20	10-07-20	₹ 0.00	₹ 0.00							
18		Wendor Approval	2 days	11-07-20	13-07-20	₹ 0.00	₹ 0.00							
19		Factory Inspection from KWA with 3rd party Inspection and Despatch Clearance from KWA	5 days	15-07-20	20-07-20	₹ 0.00	₹ 0.00							
20		DI K9 Pipes	5 days	15-07-20	20-07-20	₹ 0.00	₹ 0.00							
21		OHSR	19 days	02-07-20	23-07-20	₹ 0.00	₹ 0.00							
22		Clearing Jungles	2 days	02-07-20	03-07-20	₹ 0.00	₹ 0.00							
23		Soil Investigation	1 day	04-07-20	04-07-20	₹ 0.00	₹ 0.00							
24		Submission of Design from KWA - 54 LL OHSR	1 day	17-07-20	17-07-20	₹ 0.00	₹ 0.00							
25		Design Approval from KWA - 54 LL OHSR	5 days	18-07-20	23-07-20	₹ 0.00	₹ 0.00							
26		Procurement	162 days	21-07-20	25-01-21	₹ 48,223,753.49	₹ 0.00							
27		Placing of Purchase Order by Contractor	2 days	21-07-20	22-07-20	₹ 0.00	₹ 0.00							
28		PO-250mm,100mm,350mm DI K9 pipes	2 days	21-07-20	22-07-20	₹ 0.00	₹ 0.00							
29		Supply of Materials	160 days	23-07-20	25-01-21	₹ 48,223,753.49	₹ 0.00							
30		Supply - CWGM-250mm DI K9-Vettikuzhy jn to low le	25 days	27-07-20	24-08-20	₹ 6,625,983.50	₹ 0.00							
31		Supply - CWGM-250mm DI K9-Peelarmuzhy Anganva	25 days	23-07-20	20-08-20	₹ 23,802,400.83	₹ 0.00							
32		Supply - CWGM-100mm DI K9-Peelarmuzhy Anganva	25 days	28-12-20	25-01-21	₹ 511,931.34	₹ 0.00							
33		Supply - CWGM-350mm DI K9-Vettikuzhi jn to Peelar	25 days	28-12-20	25-01-21	₹ 7,170,479.98	₹ 0.00							
34		Supply - 20LL OHSR	25 days	23-07-20	20-08-20	₹ 5,679,041.40	₹ 0.00							
35		Supply - 14LL OHSR	25 days	23-07-20	20-08-20	₹ 3,803,757.96	₹ 0.00							
36		Supply - 1LL OHSR	25 days	23-07-20	20-08-20	₹ 502,621.88	₹ 0.00							
37		Fire hydrant	25 days	23-07-20	20-08-20	₹ 127,536.60	₹ 0.00							

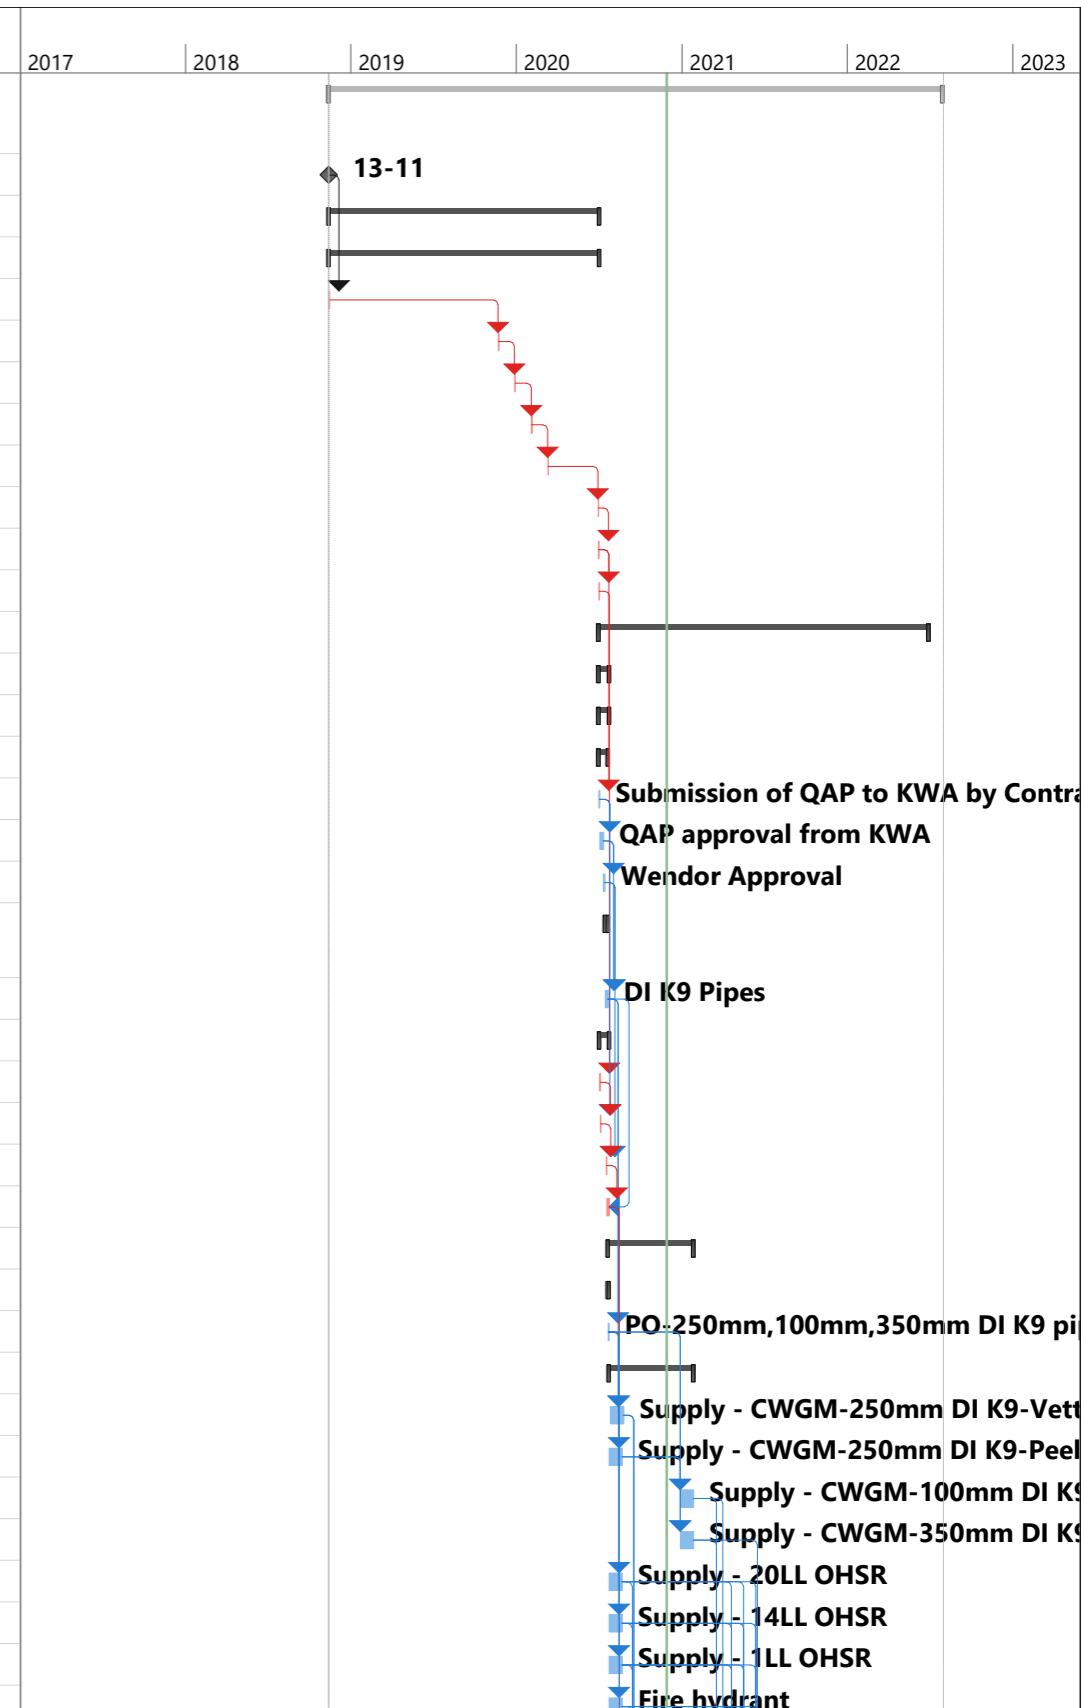

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Year						
								2017	2018	2019	2020	2021	2022	2023
38		Site Inspection by KWA Engineers	2 days	25-08-20	26-08-20	₹ 0.00	₹ 0.00							
39		Site Inspection-250mm,100mm,350mm DI K9 pipes	2 days	25-08-20	26-08-20	₹ 0.00	₹ 0.00							
40		Construction	604 days	24-07-20	28-06-22	₹ 113,840,169.59	₹ 0.00							
41		20 LL OHSR	375 days	24-07-20	04-10-21	₹ 42,969,588.48	₹ 0.00							
42		Foundation	57 days	24-07-20	28-09-20	₹ 1,734,185.91	₹ 0.00							
43		Demolition & Set Out	1 day	24-07-20	24-07-20	₹ 368,582.88	₹ 0.00							
44		Earthwork including valve chamber 2 nos	7 days	25-07-20	01-08-20	₹ 1,359,356.40	₹ 0.00							
45		Backfilling	2 days	26-09-20	28-09-20	₹ 6,246.63	₹ 0.00							
46		Substructure up to Plinth Level	66 days	29-07-20	13-10-20	₹ 16,702,517.97	₹ 0.00							
47		PCC	6 days	29-07-20	04-08-20	₹ 508,231.85	₹ 0.00							
48		FOOTING TYPE1	25 days	21-08-20	18-09-20	₹ 3,976,302.65	₹ 0.00							
49		FOOTING TYPE 2	25 days	24-08-20	21-09-20	₹ 3,976,122.47	₹ 0.00							
50		Column Pedestal/Neck Column	15 days	09-09-20	25-09-20	₹ 4,071,043.91	₹ 0.00							
51		Plinth Beam	20 days	21-09-20	13-10-20	₹ 4,170,817.09	₹ 0.00							
52		Super Structure	221 days	14-10-20	28-06-21	₹ 17,857,458.81	₹ 0.00							
53		Ground Floor up to First Brace Beam Level	40 days	14-10-20	28-11-20	₹ 1,918,200.27	₹ 0.00							
54		RCC columns up to plinth	25 days	14-10-20	11-11-20	₹ 838,189.43	₹ 0.00							
55		Brace beam and Slab at first brace level	25 days	31-10-20	28-11-20	₹ 1,080,010.84	₹ 0.00							
56		First Floor up to Second Brace Level	40 days	02-12-20	16-01-21	₹ 1,918,067.67	₹ 0.00							
57		RCC Coloums and stair case	25 days	02-12-20	30-12-20	₹ 838,066.29	₹ 0.00							
58		Brace beam and Slab at second brace level	25 days	19-12-20	16-01-21	₹ 1,080,001.38	₹ 0.00							
59		Second Floor up to Third Brace Level	40 days	20-01-21	06-03-21	₹ 1,918,070.04	₹ 0.00							
60		RCC coloums and Stair case upto third brace	25 days	20-01-21	17-02-21	₹ 838,069.85	₹ 0.00							
61		Brace beams and Slab at third brace level	25 days	06-02-21	06-03-21	₹ 1,080,000.19	₹ 0.00							
62		Third Floor up to Floor Slab of OHSR	40 days	10-03-21	24-04-21	₹ 5,647,903.53	₹ 0.00							
63		RCC coloums up to floorslab bottom, staircase	25 days	10-03-21	07-04-21	₹ 838,065.10	₹ 0.00							
64		Floor Beam and floor Slab and balcony slab	25 days	27-03-21	24-04-21	₹ 4,809,838.43	₹ 0.00							
65		Inter Connection Works	21 days	07-04-21	30-04-21	₹ 807,313.78	₹ 0.00							
66		M.S pipes, CI D/F pipes,valves, specials,cowls,M:	1 day	07-04-21	07-04-21	₹ 214,318.78	₹ 0.00							
67		fabrication of pipes, flanges, m.s ladder,	1 day	07-04-21	07-04-21	₹ 480,115.62	₹ 0.00							
68		providing of pipes , valves and specials , etc all	20 days	08-04-21	30-04-21	₹ 112,879.38	₹ 0.00							
69		Fourth Floor up to Roof Slab	50 days	01-05-21	28-06-21	₹ 5,647,903.53	₹ 0.00							
70		rcc colums inside tank ,side walls up to roof bea	25 days	01-05-21	29-05-21	₹ 838,065.11	₹ 0.00							
71		roof Beam and roof Slab	25 days	31-05-21	28-06-21	₹ 4,809,838.43	₹ 0.00							
72		Finishing Works	178 days	26-01-21	20-08-21	₹ 2,090,406.94	₹ 0.00							
73		Ground Floor up to First Brace Level	25 days	26-01-21	23-02-21	₹ 298,069.22	₹ 0.00							
74		Ceiling plaster	10 days	26-01-21	05-02-21	₹ 291,067.35	₹ 0.00							
75		Column plastering	10 days	08-02-21	18-02-21	₹ 6,655.82	₹ 0.00							
76		Surface Paintinig	5 days	12-02-21	17-02-21	₹ 346.05	₹ 0.00							
77		Hand Rail	3 days	20-02-21	23-02-21	₹ 0.00	₹ 0.00							

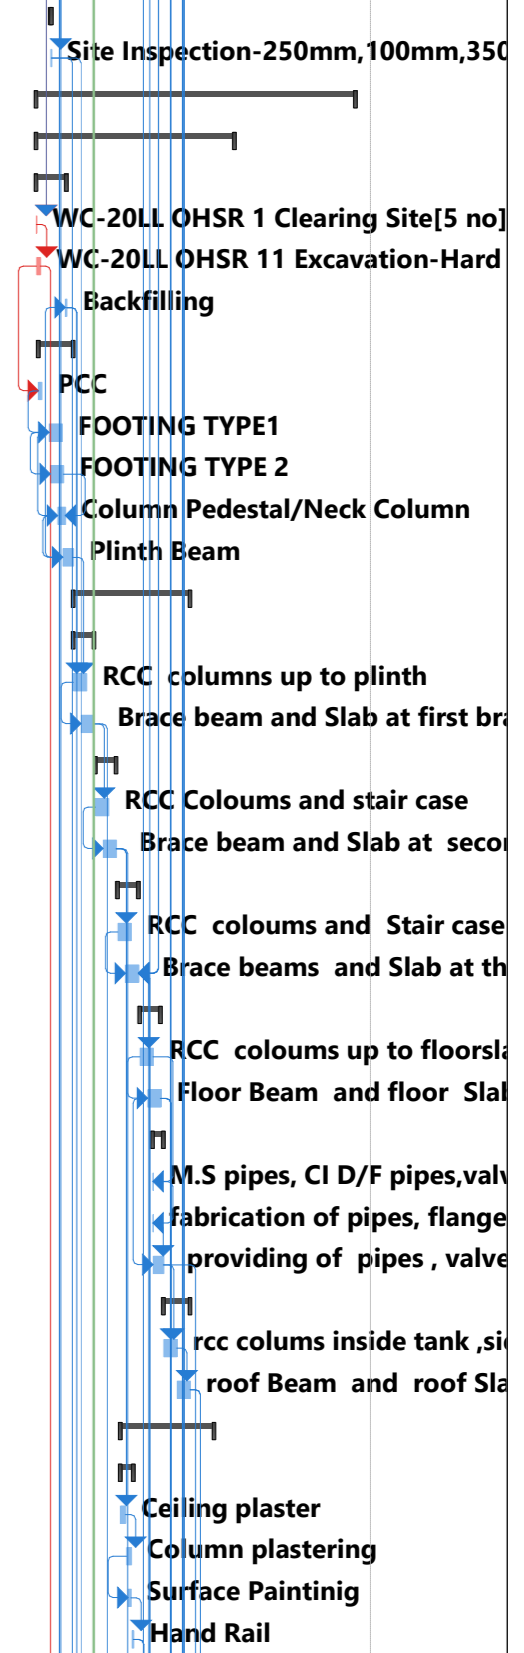

Project: WRD025-03-02-WSS to Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	2017	2018	2019	2020	2021	2022	2023
78		First Floor up to Second Brace Level	25 days	16-03-21	13-04-21	₹ 245,425.61	₹ 0.00							
79		Ceiling plaster	10 days	16-03-21	26-03-21	₹ 238,428.51	₹ 0.00							
80		Column plastering	10 days	29-03-21	08-04-21	₹ 6,651.05	₹ 0.00							
81		Surface Paintinig	5 days	02-04-21	07-04-21	₹ 346.05	₹ 0.00							
82		Hand Rail	3 days	10-04-21	13-04-21	₹ 0.00	₹ 0.00							
83		Second Floor up to Third Brace Level	25 days	04-05-21	01-06-21	₹ 245,425.61	₹ 0.00							
84		Ceiling plaster	10 days	04-05-21	14-05-21	₹ 238,428.51	₹ 0.00							
85		Column plastering	10 days	17-05-21	27-05-21	₹ 6,651.05	₹ 0.00							
86		Surface Paintinig	5 days	21-05-21	26-05-21	₹ 346.05	₹ 0.00							
87		Hand Rail	3 days	29-05-21	01-06-21	₹ 0.00	₹ 0.00							
88		Third Floor up to Floor Slab of Reservoir	30 days	07-07-21	10-08-21	₹ 364,466.00	₹ 0.00							
89		Ceiling plaster	15 days	07-07-21	23-07-21	₹ 238,428.51	₹ 0.00							
90		Column plastering	10 days	26-07-21	05-08-21	₹ 125,713.07	₹ 0.00							
91		Surface Paintinig	5 days	30-07-21	04-08-21	₹ 324.42	₹ 0.00							
92		Hand Rail	3 days	07-08-21	10-08-21	₹ 0.00	₹ 0.00							
93		Reservoir Inside Below Roof Slab	21 days	28-07-21	20-08-21	₹ 656,595.64	₹ 0.00							
94		Ceiling plaster,column inside	10 days	28-07-21	07-08-21	₹ 233,828.09	₹ 0.00							
95		Wall Plastering	10 days	10-08-21	20-08-21	₹ 125,709.38	₹ 0.00							
96		Floor Plastering	5 days	10-08-21	14-08-21	₹ 4,541.45	₹ 0.00							
97		roof Slab	5 days	16-08-21	20-08-21	₹ 292,516.72	₹ 0.00							
98		Reservor Roof Slab	10 days	10-08-21	20-08-21	₹ 280,424.86	₹ 0.00							
99		Water Proofing	10 days	10-08-21	20-08-21	₹ 280,424.86	₹ 0.00							
100		Finishing Outside Works	49 days	09-08-21	04-10-21	₹ 4,585,018.84	₹ 0.00							
101		Exterior South Side of Reservoir	21 days	21-08-21	14-09-21	₹ 1,206,281.75	₹ 0.00							
102		Erection of scaffolding	2 days	21-08-21	23-08-21	₹ 0.00	₹ 0.00							
103		Plastering	10 days	25-08-21	04-09-21	₹ 1,007,041.57	₹ 0.00							
104		Surface Paintinig	5 days	08-09-21	13-09-21	₹ 199,240.18	₹ 0.00							
105		Hand Rail	3 days	08-09-21	10-09-21	₹ 0.00	₹ 0.00							
106		Dismantling of scaffolding	1 day	14-09-21	14-09-21	₹ 0.00	₹ 0.00							
107		Exterior North Side of Reservoir	20 days	21-08-21	13-09-21	₹ 199,735.59	₹ 0.00							
108		Erection of scaffolding	2 days	21-08-21	23-08-21	₹ 0.00	₹ 0.00							
109		Plastering	10 days	25-08-21	04-09-21	₹ 498.06	₹ 0.00							
110		Surface Paintinig	5 days	08-09-21	13-09-21	₹ 199,237.53	₹ 0.00							
111		Hand Rail	3 days	08-09-21	10-09-21	₹ 0.00	₹ 0.00							
112		Dismantling of scaffolding	1 day	11-09-21	11-09-21	₹ 0.00	₹ 0.00							
113		Exterior East Side of Reservoir	19 days	13-09-21	04-10-21	₹ 1,208,138.78	₹ 0.00							
114		Erection of scaffolding	2 days	13-09-21	14-09-21	₹ 0.00	₹ 0.00							
115		Plastering	10 days	16-09-21	27-09-21	₹ 1,007,006.25	₹ 0.00							
116		Surface Paintinig	3 days	30-09-21	02-10-21	₹ 201,132.53	₹ 0.00							
117		Hand Rail	3 days	30-09-21	02-10-21	₹ 0.00	₹ 0.00							

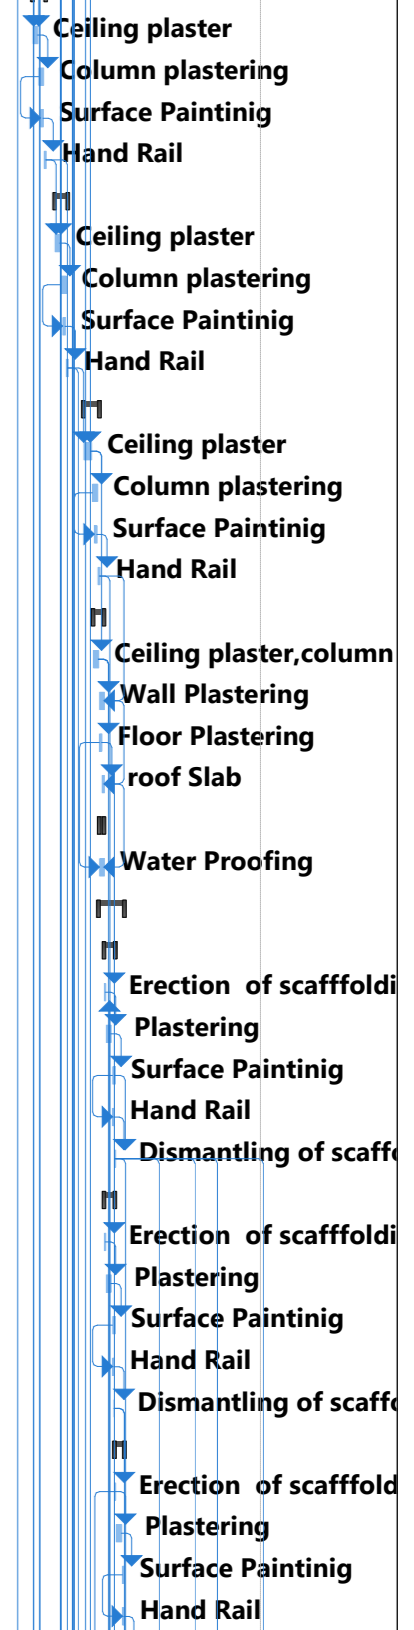

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Year								
								2017	2018	2019	2020	2021	2022	2023		
118		Dismantling of scaffolding	1 day	04-10-21	04-10-21	₹ 0.00	₹ 0.00									
119		Exterior West Side of Reservoir	19 days	13-09-21	04-10-21	₹ 1,208,138.78	₹ 0.00									
120		Erection of scaffolding	2 days	13-09-21	14-09-21	₹ 0.00	₹ 0.00									
121		Plastering	10 days	16-09-21	27-09-21	₹ 1,007,006.25	₹ 0.00									
122		Surface Paintinig	3 days	30-09-21	02-10-21	₹ 201,132.53	₹ 0.00									
123		Hand Rail	3 days	30-09-21	02-10-21	₹ 0.00	₹ 0.00									
124		Dismantling of scaffolding	1 day	04-10-21	04-10-21	₹ 0.00	₹ 0.00									
125		Testing and Commissioning	48 days	09-08-21	02-10-21	₹ 762,723.94	₹ 0.00									
126		Testing, commissioning	1 day	09-08-21	09-08-21	₹ 0.00	₹ 0.00									
127		anchor block, lightning arrester & level indicator	3 days	30-09-21	02-10-21	₹ 762,723.94	₹ 0.00									
128		20LL OHSR -Valve Chambers and Anchor Blocks	11 days	03-08-20	14-08-20	₹ 777,870.02	₹ 0.00									
129		EXCAVATION	3 days	03-08-20	05-08-20	₹ 88,543.91	₹ 0.00									
130		PCC	2 days	06-08-20	07-08-20	₹ 34,524.24	₹ 0.00									
131		Centering and Shuttering	2 days	08-08-20	10-08-20	₹ 145,076.60	₹ 0.00									
132		RCC works	3 days	08-08-20	11-08-20	₹ 509,725.27	₹ 0.00									
133		Backfilling	2 days	12-08-20	13-08-20	₹ 0.00	₹ 0.00									
134		Manhole Cover	2 days	13-08-20	14-08-20	₹ 0.00	₹ 0.00									
135		20LL OHSR- Compound Wall	21 days	14-08-20	07-09-20	₹ 978,408.54	₹ 0.00									
136		Earth work	5 days	14-08-20	19-08-20	₹ 422,476.35	₹ 0.00									
137		PCC	3 days	20-08-20	22-08-20	₹ 46,295.28	₹ 0.00									
138		RCC pillars	5 days	24-08-20	28-08-20	₹ 63,858.72	₹ 0.00									
139		Finishing works	8 days	29-08-20	07-09-20	₹ 445,778.19	₹ 0.00									
140		Plastering	4 days	29-08-20	02-09-20	₹ 402,379.77	₹ 0.00									
141		Painting	4 days	03-09-20	07-09-20	₹ 43,398.42	₹ 0.00									
142		14 LL OHSR	375 days	20-08-20	30-10-21	₹ 22,991,815.68	₹ 0.00									
143		Foundation	57 days	20-08-20	24-10-20	₹ 535,979.61	₹ 0.00									
144		Set Out	1 day	20-08-20	20-08-20	₹ 3,941.05	₹ 0.00									
145		Earthwork including valve chamber 2 nos	7 days	21-08-20	28-08-20	₹ 528,871.76	₹ 0.00									
146		Backfilling	2 days	23-10-20	24-10-20	₹ 3,166.80	₹ 0.00									
147		Substructure up to Plinth Level	66 days	25-08-20	09-11-20	₹ 4,232,652.83	₹ 0.00									
148		PCC	6 days	25-08-20	31-08-20	₹ 202,592.04	₹ 0.00									
149		FOOTING TYPE1	25 days	17-09-20	15-10-20	₹ 927,989.64	₹ 0.00									
150		FOOTING TYPE 2	25 days	19-09-20	17-10-20	₹ 927,718.65	₹ 0.00									
151		Column Pedestal/Neck Column	15 days	06-10-20	22-10-20	₹ 1,155,533.97	₹ 0.00									
152		Plinth Beam	20 days	17-10-20	09-11-20	₹ 1,018,818.53	₹ 0.00									
153		Super Structure	221 days	10-11-20	24-07-21	₹ 15,013,808.64	₹ 0.00									
154		Ground Floor up to First Brace Beam Level	40 days	10-11-20	25-12-20	₹ 2,466,987.17	₹ 0.00									
155		RCC columns up to plinth	25 days	10-11-20	08-12-20	₹ 1,209,350.93	₹ 0.00									
156		Brace beam and Slab at first brace level	25 days	27-11-20	25-12-20	₹ 1,257,636.23	₹ 0.00									
157		First Floor up to Second Brace Level	40 days	29-12-20	12-02-21	₹ 2,374,876.86	₹ 0.00									

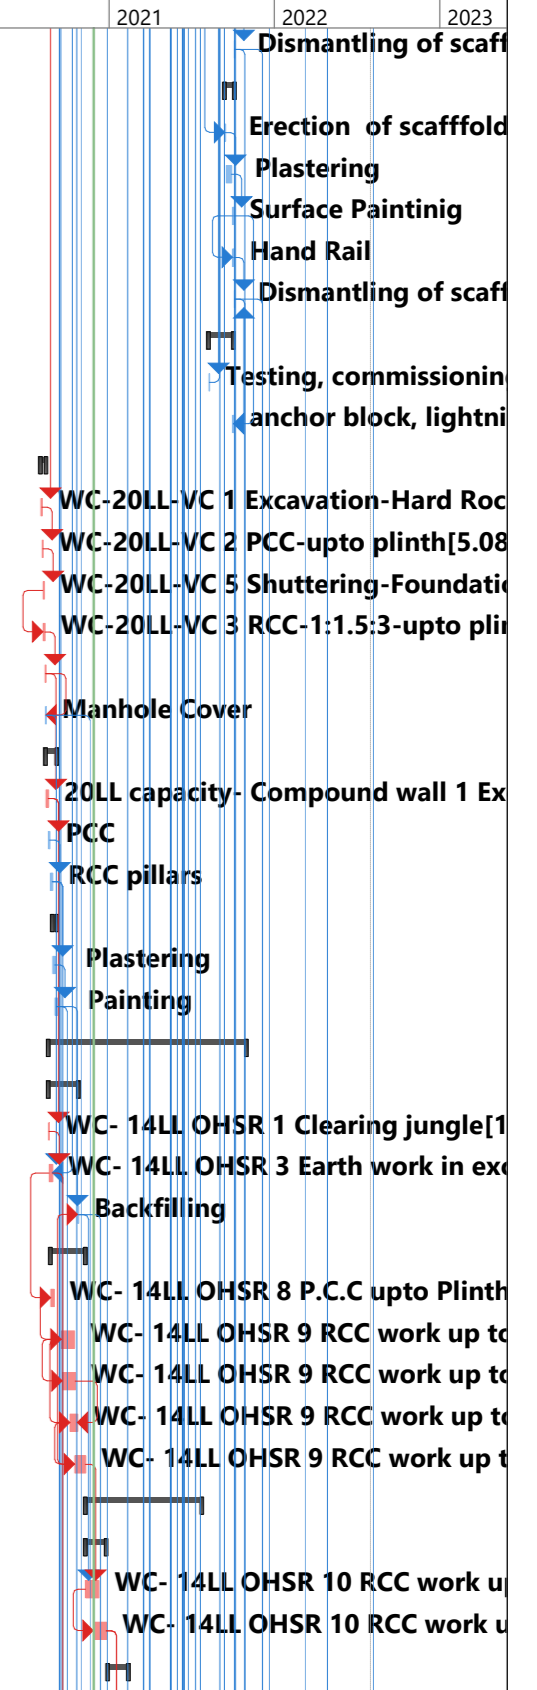

Project: WRD025-03-02-WSS to Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	2017	2018	2019	2020	2021	2022	2023
198		roof Slab	5 days	11-09-21	16-09-21	₹ 295,807.21	₹ 0.00							
199		Reservor Roof Slab	10 days	06-09-21	16-09-21	₹ 0.00	₹ 0.00							
200		Water Proofing	10 days	06-09-21	16-09-21	₹ 0.00	₹ 0.00							
201		Finishing Outside Works	49 days	04-09-21	30-10-21	₹ 2,144,153.76	₹ 0.00							
202		Exterior South Side of Reservoir	21 days	17-09-21	11-10-21	₹ 498,893.02	₹ 0.00							
203		Erection of scaffolding	2 days	17-09-21	18-09-21	₹ 0.00	₹ 0.00							
204		Plastering	10 days	21-09-21	01-10-21	₹ 316,338.71	₹ 0.00							
205		Surface Paintinig	5 days	05-10-21	09-10-21	₹ 158,253.07	₹ 0.00							
206		Hand Rail	3 days	05-10-21	07-10-21	₹ 24,301.24	₹ 0.00							
207		Dismantling of scaffolding	1 day	11-10-21	11-10-21	₹ 0.00	₹ 0.00							
208		Exterior North Side of Reservoir	20 days	17-09-21	09-10-21	₹ 497,006.37	₹ 0.00							
209		Erection of scaffolding	2 days	17-09-21	18-09-21	₹ 0.00	₹ 0.00							
210		Plastering	10 days	21-09-21	01-10-21	₹ 314,457.36	₹ 0.00							
211		Surface Paintinig	5 days	05-10-21	09-10-21	₹ 158,247.77	₹ 0.00							
212		Hand Rail	3 days	05-10-21	07-10-21	₹ 24,301.24	₹ 0.00							
213		Dismantling of scaffolding	1 day	08-10-21	08-10-21	₹ 0.00	₹ 0.00							
214		Exterior East Side of Reservoir	19 days	09-10-21	30-10-21	₹ 498,901.37	₹ 0.00							
215		Erection of scaffolding	2 days	09-10-21	11-10-21	₹ 0.00	₹ 0.00							
216		Plastering	10 days	13-10-21	23-10-21	₹ 314,457.36	₹ 0.00							
217		Surface Paintinig	3 days	27-10-21	29-10-21	₹ 160,142.77	₹ 0.00							
218		Hand Rail	3 days	27-10-21	29-10-21	₹ 24,301.24	₹ 0.00							
219		Dismantling of scaffolding	1 day	30-10-21	30-10-21	₹ 0.00	₹ 0.00							
220		Exterior West Side of Reservoir	19 days	09-10-21	30-10-21	₹ 506,409.77	₹ 0.00							
221		Erection of scaffolding	2 days	09-10-21	11-10-21	₹ 0.00	₹ 0.00							
222		Plastering	10 days	13-10-21	23-10-21	₹ 321,965.76	₹ 0.00							
223		Surface Paintinig	3 days	27-10-21	29-10-21	₹ 160,142.77	₹ 0.00							
224		Hand Rail	3 days	27-10-21	29-10-21	₹ 24,301.24	₹ 0.00							
225		Dismantling of scaffolding	1 day	30-10-21	30-10-21	₹ 0.00	₹ 0.00							
226		Testing and Commissioning	48 days	04-09-21	29-10-21	₹ 142,943.22	₹ 0.00							
227		Testing, commissioning	1 day	04-09-21	04-09-21	₹ 0.00	₹ 0.00							
228		anchor block, lightning arrester & level indicator	3 days	27-10-21	29-10-21	₹ 142,943.22	₹ 0.00							
229		14LL OHSR -Valve Chambers and Anchor Blocks	11 days	29-08-20	10-09-20	₹ 652,646.40	₹ 0.00							
230		EXCAVATION	3 days	29-08-20	01-09-20	₹ 39,602.00	₹ 0.00							
231		PCC	2 days	02-09-20	03-09-20	₹ 30,582.50	₹ 0.00							
232		Centering and Shuttering	2 days	04-09-20	05-09-20	₹ 133,448.16	₹ 0.00							
233		RCC works	3 days	04-09-20	07-09-20	₹ 449,013.75	₹ 0.00							
234		Backfilling	2 days	08-09-20	09-09-20	₹ 0.00	₹ 0.00							
235		Manhole Cover	2 days	09-09-20	10-09-20	₹ 0.00	₹ 0.00							
236		14LL OHSR -Compound Wall	21 days	10-09-20	03-10-20	₹ 705,311.16	₹ 0.00							
237		Earth work	5 days	10-09-20	15-09-20	₹ 353,171.77	₹ 0.00							

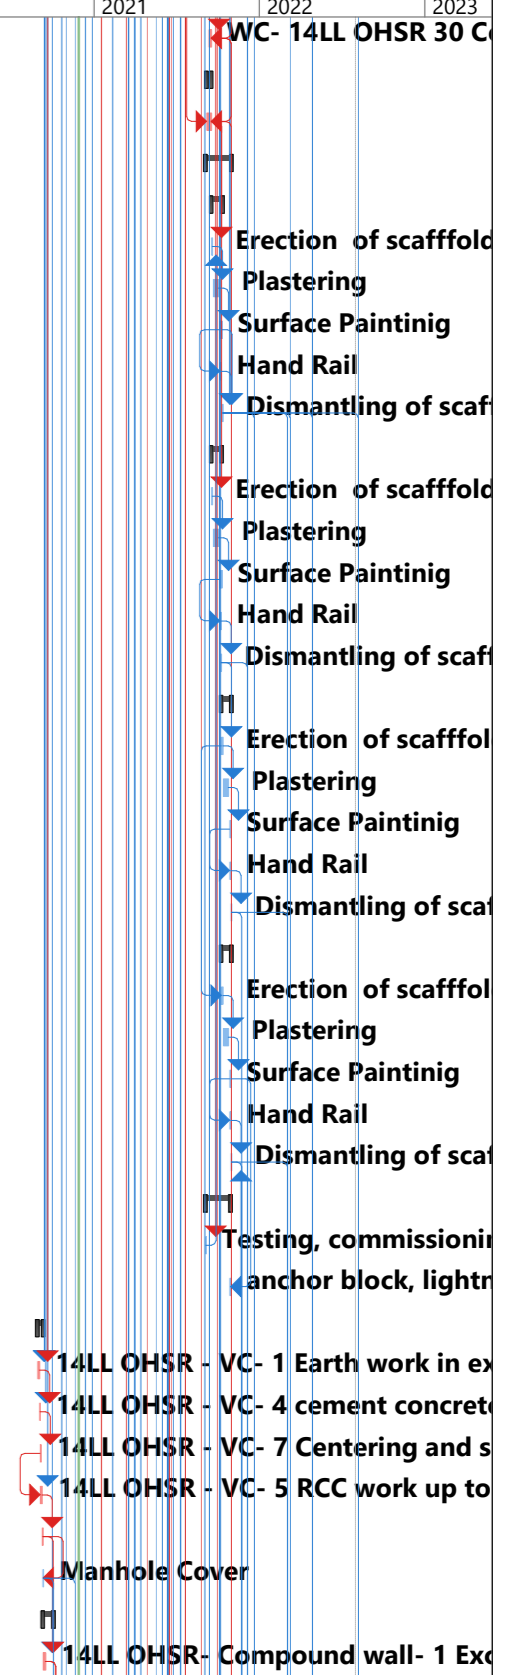

Project: WRD025-03-02-WSS to Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Gantt Chart								
								2017	2018	2019	2020	2021	2022	2023		
238		PCC	3 days	16-09-20	18-09-20	₹ 0.00	₹ 0.00									
239		RCC pillars	5 days	19-09-20	24-09-20	₹ 210,857.54	₹ 0.00									
240		Finishing works	8 days	25-09-20	03-10-20	₹ 141,281.85	₹ 0.00									
241		Plastering	4 days	25-09-20	29-09-20	₹ 104,270.77	₹ 0.00									
242		Painting	4 days	30-09-20	03-10-20	₹ 37,011.08	₹ 0.00									
243		1 LL OHSR	375 days	16-09-20	26-11-21	₹ 2,994,191.90	₹ 0.00									
244		Foundation	57 days	16-09-20	20-11-20	₹ 166,354.97	₹ 0.00									
245		Set Out	1 day	16-09-20	16-09-20	₹ 68,082.62	₹ 0.00									
246		Earthwork including valve chamber 2 nos	7 days	17-09-20	24-09-20	₹ 97,099.73	₹ 0.00									
247		Backfilling	2 days	19-11-20	20-11-20	₹ 1,172.61	₹ 0.00									
248		Substructure up to Plinth Level	66 days	21-09-20	05-12-20	₹ 452,679.55	₹ 0.00									
249		PCC	6 days	21-09-20	26-09-20	₹ 27,864.05	₹ 0.00									
250		FOOTING TYPE1	25 days	14-10-20	11-11-20	₹ 109,459.37	₹ 0.00									
251		FOOTING TYPE 2	25 days	16-10-20	13-11-20	₹ 103,057.13	₹ 0.00									
252		Column Pedestal/Neck Column	15 days	02-11-20	18-11-20	₹ 109,859.01	₹ 0.00									
253		Plinth Beam	20 days	13-11-20	05-12-20	₹ 102,439.99	₹ 0.00									
254		Super Structure	221 days	07-12-20	20-08-21	₹ 1,747,525.51	₹ 0.00									
255		Ground Floor up to First Brace Beam Level	40 days	07-12-20	21-01-21	₹ 116,307.93	₹ 0.00									
256		RCC columns up to plinth	25 days	07-12-20	04-01-21	₹ 498.06	₹ 0.00									
257		Brace beam and Slab at first brace level	25 days	24-12-20	21-01-21	₹ 115,809.87	₹ 0.00									
258		First Floor up to Second Brace Level	40 days	25-01-21	11-03-21	₹ 376,543.07	₹ 0.00									
259		RCC Coloums and stair case	25 days	25-01-21	22-02-21	₹ 260,750.67	₹ 0.00									
260		Brace beam and Slab at second brace level	25 days	11-02-21	11-03-21	₹ 115,792.40	₹ 0.00									
261		Second Floor up to Third Brace Level	40 days	15-03-21	29-04-21	₹ 376,437.28	₹ 0.00									
262		RCC coloums and Stair case upto third brace	25 days	15-03-21	12-04-21	₹ 260,644.89	₹ 0.00									
263		Brace beams and Slab at third brace level	25 days	01-04-21	29-04-21	₹ 115,792.40	₹ 0.00									
264		Third Floor up to Floor Slab of OHSR	40 days	03-05-21	17-06-21	₹ 380,705.42	₹ 0.00									
265		RCC coloums up to floorslab bottom, staircase	25 days	03-05-21	31-05-21	₹ 262,782.79	₹ 0.00									
266		Floor Beam and floor Slab and balcony slab	25 days	20-05-21	17-06-21	₹ 117,922.63	₹ 0.00									
267		Inter Connection Works	21 days	31-05-21	23-06-21	₹ 75,825.36	₹ 0.00									
268		M.S pipes, CI D/F pipes,valves, specials,cowls,M	1 day	31-05-21	31-05-21	₹ 60,332.76	₹ 0.00									
269		fabrication of pipes, flanges, m.s ladder,	1 day	31-05-21	31-05-21	₹ 6,917.14	₹ 0.00									
270		providing of pipes , valves and specials , etc all	20 days	01-06-21	23-06-21	₹ 8,575.46	₹ 0.00									
271		Fourth Floor up to Roof Slab	50 days	24-06-21	20-08-21	₹ 421,706.45	₹ 0.00									
272		rcc colums inside tank ,side walls up to roof bea	25 days	24-06-21	22-07-21	₹ 279,585.06	₹ 0.00									
273		roof Beam and roof Slab	25 days	23-07-21	20-08-21	₹ 142,121.39	₹ 0.00									
274		Finishing Works	178 days	20-03-21	13-10-21	₹ 223,237.89	₹ 0.00									
275		Ground Floor up to First Brace Level	25 days	20-03-21	17-04-21	₹ 36,294.97	₹ 0.00									
276		Ceiling plaster	10 days	20-03-21	31-03-21	₹ 3,910.50	₹ 0.00									
277		Column plastering	10 days	02-04-21	13-04-21	₹ 20,319.39	₹ 0.00									

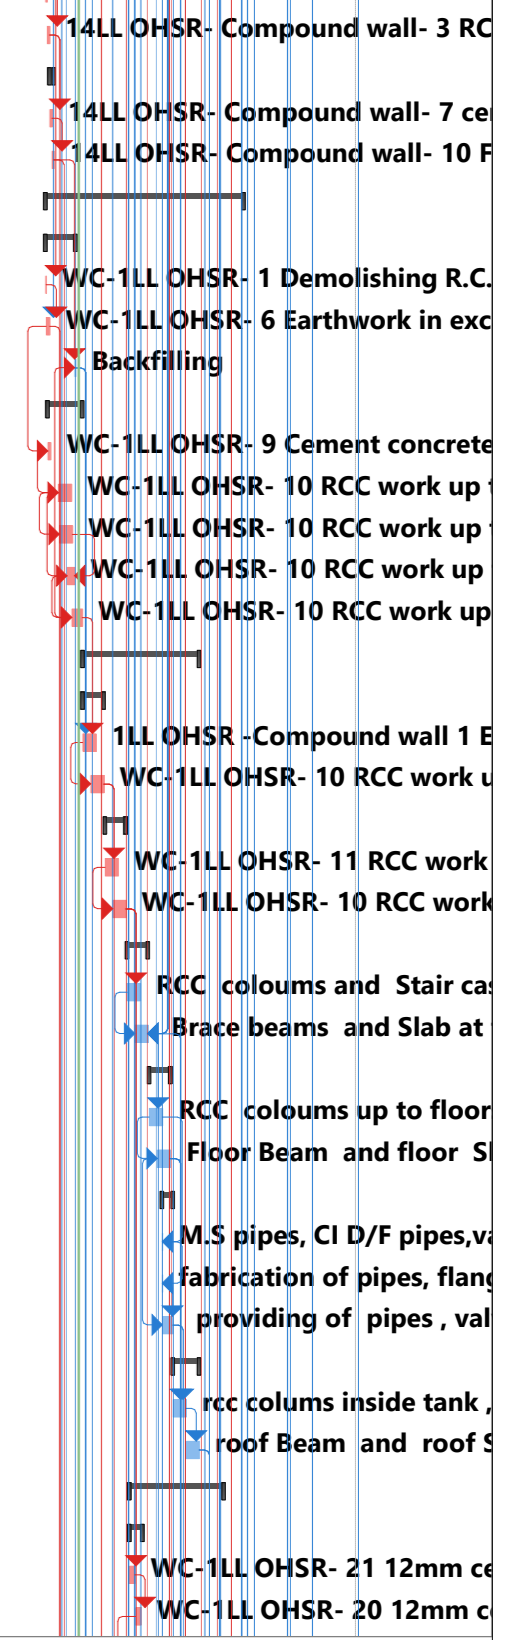

Project: WRD025-03-02-WSS to Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Timeline								
								2017	2018	2019	2020	2021	2022	2023		
358		Manhole Cover	2 days	12-11-20	13-11-20	₹ 0.00	₹ 0.00									
359		Laying - Ch: 0/550 to Ch: 1/920	87 days	20-11-20	01-03-21	₹ 881,682.53	₹ 0.00									
360		Pipe Laying	87 days	20-11-20	01-03-21	₹ 881,682.53	₹ 0.00									
361		Demolishing Concrete/Bitumen and Excavatic	26 days	20-11-20	19-12-20	₹ 614,995.40	₹ 0.00									
362		Laying of pipes	26 days	22-12-20	20-01-21	₹ 187,274.87	₹ 0.00									
363		Backfilling	20 days	01-01-21	23-01-21	₹ 7,671.30	₹ 0.00									
364		Road reformation	26 days	30-01-21	01-03-21	₹ 1,315.58	₹ 0.00									
365		Valve Chambers and Anchor Blocks	11 days	23-12-20	04-01-21	₹ 70,425.37	₹ 0.00									
366		Excavation	3 days	23-12-20	25-12-20	₹ 2,125.09	₹ 0.00									
367		PCC	2 days	26-12-20	28-12-20	₹ 7,632.31	₹ 0.00									
368		Centering and Shuttering	2 days	29-12-20	30-12-20	₹ 12,008.61	₹ 0.00									
369		RCC works	3 days	29-12-20	31-12-20	₹ 48,659.37	₹ 0.00									
370		Backfilling	2 days	01-01-21	02-01-21	₹ 0.00	₹ 0.00									
371		Manhole Cover	2 days	02-01-21	04-01-21	₹ 0.00	₹ 0.00									
372		Laying - Ch: 1/920 to Ch: 2/100	65 days	23-01-21	08-04-21	₹ 849,784.72	₹ 0.00									
373		Pipe Laying	65 days	23-01-21	08-04-21	₹ 849,784.72	₹ 0.00									
374		Demolishing Concrete/Bitumen and Excavatic	15 days	23-01-21	09-02-21	₹ 580,360.17	₹ 0.00									
375		Laying of pipes	15 days	11-02-21	27-02-21	₹ 190,017.23	₹ 0.00									
376		Backfilling	18 days	11-02-21	03-03-21	₹ 7,671.30	₹ 0.00									
377		Road reformation	26 days	10-03-21	08-04-21	₹ 1,315.58	₹ 0.00									
378		Valve Chambers and Anchor Blocks	11 days	12-02-21	24-02-21	₹ 70,420.44	₹ 0.00									
379		Excavation	3 days	12-02-21	15-02-21	₹ 2,125.09	₹ 0.00									
380		PCC	2 days	16-02-21	17-02-21	₹ 7,632.31	₹ 0.00									
381		Centering and Shuttering	2 days	18-02-21	19-02-21	₹ 12,006.07	₹ 0.00									
382		RCC works	3 days	18-02-21	20-02-21	₹ 48,656.98	₹ 0.00									
383		Backfilling	2 days	22-02-21	23-02-21	₹ 0.00	₹ 0.00									
384		Manhole Cover	2 days	23-02-21	24-02-21	₹ 0.00	₹ 0.00									
385		Pipe Bridge	104 days	12-07-21	09-11-21	₹ 147,359.42	₹ 0.00									
386		Piling	26 days	12-07-21	10-08-21	₹ 12,953.59	₹ 0.00									
387		PCC	2 days	13-08-21	14-08-21	₹ 3,330.09	₹ 0.00									
388		Pier	15 days	27-08-21	13-09-21	₹ 78,683.71	₹ 0.00									
389		Pipe Bridge	26 days	08-10-21	06-11-21	₹ 51,963.72	₹ 0.00									
390		Laying of pipes	2 days	08-11-21	09-11-21	₹ 428.30	₹ 0.00									
391		Clear Water Gravity Main 250mm DI K9-Peelarmuzhy	339 days	28-12-20	26-01-22	₹ 8,329,938.62	₹ 0.00									
392		Pipe Laying	309 days	28-12-20	22-12-21	₹ 8,182,776.98	₹ 0.00									
393		Laying - Ch: 0/000 to Ch: 1/550	65 days	28-12-20	12-03-21	₹ 1,605,310.87	₹ 0.00									
394		Pipe Laying	65 days	28-12-20	12-03-21	₹ 1,605,310.87	₹ 0.00									
395		Demolishing Concrete/Bitumen and Excavatic	15 days	28-12-20	13-01-21	₹ 759,333.85	₹ 0.00									
396		Laying of pipes	15 days	15-01-21	01-02-21	₹ 324,957.91	₹ 0.00									
397		Backfilling	18 days	15-01-21	04-02-21	₹ 13,407.77	₹ 0.00									

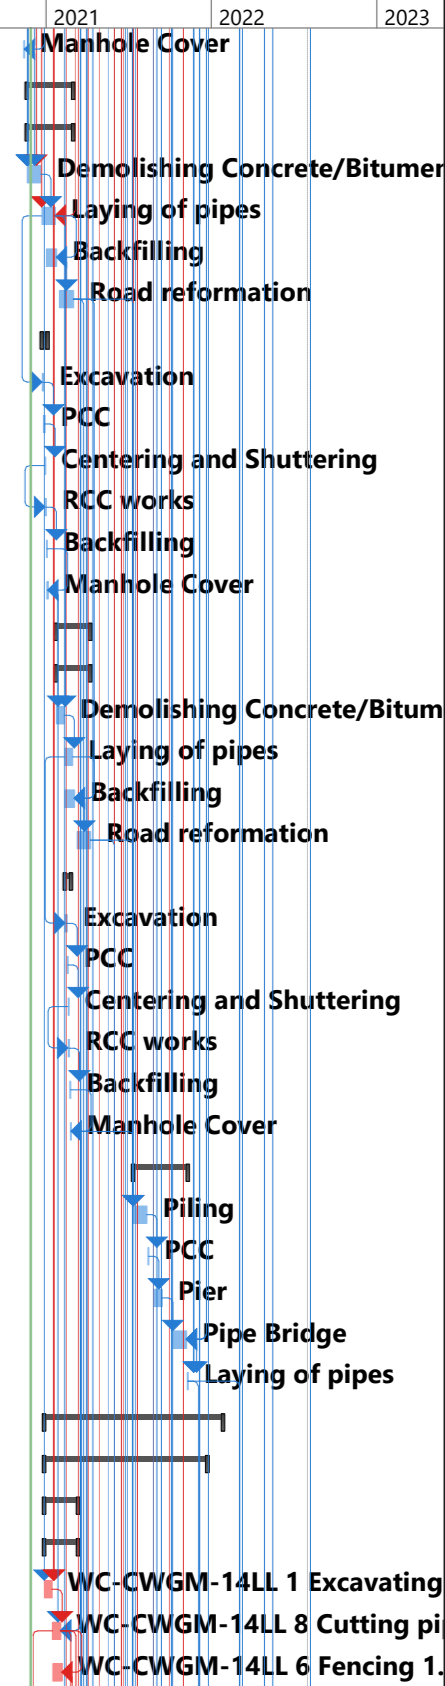

Project: WRD025-03-02-WSS to Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Year								
								2017	2018	2019	2020	2021	2022	2023		
438		Valve Chambers and Anchor Blocks	13 days	07-06-21	21-06-21	₹ 198,485.88	₹ 0.00									
439		Excavation	3 days	07-06-21	09-06-21	₹ 1,623.75	₹ 0.00									
440		PCC	2 days	10-06-21	11-06-21	₹ 97,073.28	₹ 0.00									
441		Centering and Shuttering	2 days	12-06-21	14-06-21	₹ 21,396.69	₹ 0.00									
442		RCC works	3 days	12-06-21	15-06-21	₹ 78,392.16	₹ 0.00									
443		Backfilling	2 days	16-06-21	17-06-21	₹ 0.00	₹ 0.00									
444		Manhole Cover	2 days	19-06-21	21-06-21	₹ 0.00	₹ 0.00									
445		Laying - Ch: 5/830 to Ch: 6/055	87 days	25-06-21	04-10-21	₹ 1,285,311.21	₹ 0.00									
446		Pipe Laying	87 days	25-06-21	04-10-21	₹ 1,285,311.21	₹ 0.00									
447		Demolishing Concrete/Bitumen and Excavatic	26 days	25-06-21	24-07-21	₹ 759,251.27	₹ 0.00									
448		Laying of pipes	26 days	27-07-21	25-08-21	₹ 307,590.69	₹ 0.00									
449		Backfilling	20 days	06-08-21	28-08-21	₹ 13,406.26	₹ 0.00									
450		Road reformation	26 days	04-09-21	04-10-21	₹ 6,577.90	₹ 0.00									
451		Valve Chambers and Anchor Blocks	13 days	28-07-21	11-08-21	₹ 198,485.10	₹ 0.00									
452		Excavation	3 days	28-07-21	30-07-21	₹ 1,623.75	₹ 0.00									
453		PCC	2 days	31-07-21	02-08-21	₹ 97,073.28	₹ 0.00									
454		Centering and Shuttering	2 days	03-08-21	04-08-21	₹ 21,396.69	₹ 0.00									
455		RCC works	3 days	03-08-21	05-08-21	₹ 78,391.38	₹ 0.00									
456		Backfilling	2 days	06-08-21	07-08-21	₹ 0.00	₹ 0.00									
457		Manhole Cover	2 days	10-08-21	11-08-21	₹ 0.00	₹ 0.00									
458		Laying - Ch: 6/095 to Ch: 7/340	87 days	13-09-21	22-12-21	₹ 1,401,333.82	₹ 0.00									
459		Pipe Laying	87 days	13-09-21	22-12-21	₹ 1,401,333.82	₹ 0.00									
460		Demolishing Concrete/Bitumen and Excavatic	26 days	13-09-21	12-10-21	₹ 759,251.27	₹ 0.00									
461		Laying of pipes	26 days	14-10-21	12-11-21	₹ 423,613.30	₹ 0.00									
462		Backfilling	20 days	25-10-21	16-11-21	₹ 13,406.26	₹ 0.00									
463		Road reformation	26 days	23-11-21	22-12-21	₹ 6,577.90	₹ 0.00									
464		Valve Chambers and Anchor Blocks	11 days	15-10-21	27-10-21	₹ 198,485.10	₹ 0.00									
465		Excavation	3 days	15-10-21	18-10-21	₹ 1,623.75	₹ 0.00									
466		PCC	2 days	19-10-21	20-10-21	₹ 97,073.28	₹ 0.00									
467		Centering and Shuttering	2 days	21-10-21	22-10-21	₹ 21,396.69	₹ 0.00									
468		RCC works	3 days	21-10-21	23-10-21	₹ 78,391.38	₹ 0.00									
469		Backfilling	2 days	25-10-21	26-10-21	₹ 0.00	₹ 0.00									
470		Manhole Cover	2 days	26-10-21	27-10-21	₹ 0.00	₹ 0.00									
471		Pipe Bridge	98 days	05-10-21	26-01-22	₹ 147,161.64	₹ 0.00									
472		Piling	26 days	05-10-21	03-11-21	₹ 12,925.51	₹ 0.00									
473		PCC	2 days	06-11-21	08-11-21	₹ 3,126.21	₹ 0.00									
474		Pier	15 days	20-11-21	07-12-21	₹ 78,720.29	₹ 0.00									
475		Pipe Bridge	26 days	25-12-21	24-01-22	₹ 51,961.33	₹ 0.00									
476		Laying of pipes	2 days	25-01-22	26-01-22	₹ 428.30	₹ 0.00									
477		Clear Water Gravity Main 100mm DI K9-Peelarmuzhy	316 days	13-03-21	16-03-22	₹ 1,192,536.85	₹ 0.00									

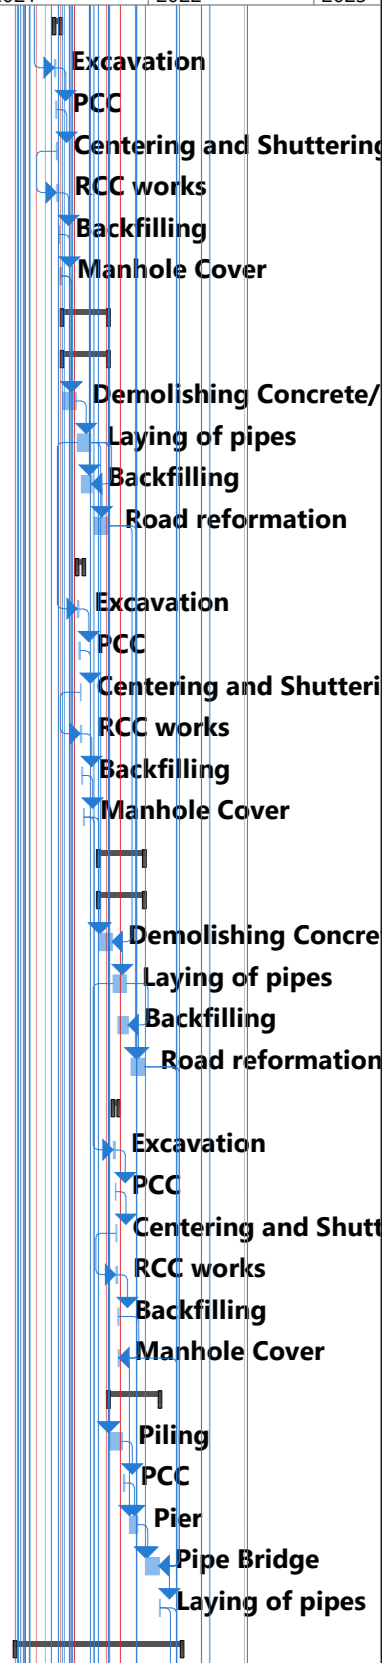

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Year								
								2017	2018	2019	2020	2021	2022	2023		
478		Pipe Laying	65 days	13-03-21	27-05-21	₹ 1,063,044.91	₹ 0.00									
479		Laying - Ch: 0/000 to Ch: 0/370	65 days	13-03-21	27-05-21	₹ 1,063,044.91	₹ 0.00									
480		Pipe Laying	65 days	13-03-21	27-05-21	₹ 1,063,044.91	₹ 0.00									
481		Demolishing Concrete/Bitumen and Excavatic	15 days	13-03-21	30-03-21	₹ 438,159.69	₹ 0.00									
482		Laying of pipes	15 days	01-04-21	17-04-21	₹ 576,004.13	₹ 0.00									
483		Backfilling	18 days	01-04-21	21-04-21	₹ 4,998.24	₹ 0.00									
484		Road reformation	26 days	28-04-21	27-05-21	₹ 0.00	₹ 0.00									
485		Valve Chambers and Anchor Blocks	11 days	02-04-21	14-04-21	₹ 43,882.85	₹ 0.00									
486		EXCAVATION	3 days	02-04-21	05-04-21	₹ 582.98	₹ 0.00									
487		PCC	2 days	06-04-21	07-04-21	₹ 4,070.23	₹ 0.00									
488		Centering and Shuttering	2 days	08-04-21	09-04-21	₹ 9,453.23	₹ 0.00									
489		RCC works	3 days	08-04-21	10-04-21	₹ 29,776.41	₹ 0.00									
490		Backfilling	2 days	12-04-21	13-04-21	₹ 0.00	₹ 0.00									
491		Manhole Cover	2 days	13-04-21	14-04-21	₹ 0.00	₹ 0.00									
492		Pipe Bridge	98 days	23-11-21	16-03-22	₹ 129,491.94	₹ 0.00									
493		Piling	26 days	23-11-21	22-12-21	₹ 2,788.59	₹ 0.00									
494		PCC	2 days	25-12-21	27-12-21	₹ 3,126.21	₹ 0.00									
495		Pier	15 days	08-01-22	25-01-22	₹ 70,973.36	₹ 0.00									
496		Pipe Bridge	26 days	12-02-22	14-03-22	₹ 51,961.33	₹ 0.00									
497		Laying of pipes	2 days	15-03-22	16-03-22	₹ 642.45	₹ 0.00									
498		Clear Water Gravity Main 350mm DI K9-Vettikuzhi jn t	340 days	28-05-21	28-06-22	₹ 2,979,775.84	₹ 0.00									
499		Pipe Laying	127 days	28-05-21	22-10-21	₹ 2,850,112.92	₹ 0.00									
500		Laying - Ch: 0/000 to Ch: 0/550	65 days	28-05-21	11-08-21	₹ 1,424,539.01	₹ 0.00									
501		Pipe Laying	65 days	28-05-21	11-08-21	₹ 1,424,539.01	₹ 0.00									
502		Demolishing Concrete/Bitumen and Excavatic	15 days	28-05-21	14-06-21	₹ 993,161.82	₹ 0.00									
503		Laying of pipes	15 days	16-06-21	02-07-21	₹ 254,458.54	₹ 0.00									
504		Backfilling	18 days	16-06-21	06-07-21	₹ 10,208.25	₹ 0.00									
505		Road reformation	26 days	13-07-21	11-08-21	₹ 0.00	₹ 0.00									
506		Valve Chambers and Anchor Blocks	18 days	17-06-21	07-07-21	₹ 166,710.41	₹ 0.00									
507		EXCAVATION	10 days	17-06-21	28-06-21	₹ 1,400.07	₹ 0.00									
508		PCC	2 days	29-06-21	30-06-21	₹ 2,582.52	₹ 0.00									
509		Centering and Shuttering	2 days	01-07-21	02-07-21	₹ 21,539.68	₹ 0.00									
510		RCC works	3 days	01-07-21	03-07-21	₹ 141,188.13	₹ 0.00									
511		Backfilling	2 days	05-07-21	06-07-21	₹ 0.00	₹ 0.00									
512		Manhole Cover	2 days	06-07-21	07-07-21	₹ 0.00	₹ 0.00									
513		Laying - Ch: 0/550 to Ch: 1/500	87 days	14-07-21	22-10-21	₹ 1,425,573.90	₹ 0.00									
514		Pipe Laying	87 days	14-07-21	22-10-21	₹ 1,425,573.90	₹ 0.00									
515		Demolishing Concrete/Bitumen and Excavatic	26 days	14-07-21	12-08-21	₹ 993,161.82	₹ 0.00									
516		Laying of pipes	26 days	14-08-21	13-09-21	₹ 255,652.47	₹ 0.00									
517		Backfilling	20 days	25-08-21	16-09-21	₹ 10,208.25	₹ 0.00									

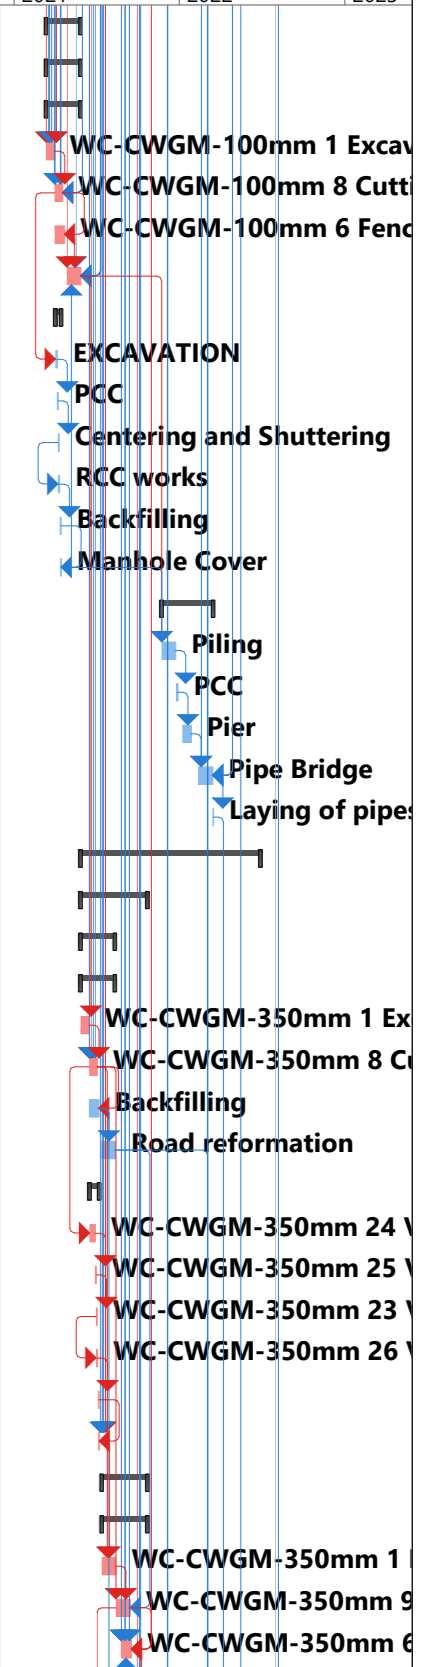

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	Year								
								2017	2018	2019	2020	2021	2022	2023		
518		Road reformation	26 days	23-09-21	22-10-21	₹ 0.00	₹ 0.00									
519		Valve Chambers and Anchor Blocks	18 days	16-08-21	04-09-21	₹ 166,551.36	₹ 0.00									
520		Excavation	10 days	16-08-21	26-08-21	₹ 1,400.07	₹ 0.00									
521		PCC	2 days	27-08-21	28-08-21	₹ 2,514.56	₹ 0.00									
522		Centering and Shuttering	2 days	30-08-21	31-08-21	₹ 21,534.33	₹ 0.00									
523		RCC works	3 days	30-08-21	01-09-21	₹ 141,102.40	₹ 0.00									
524		Backfilling	2 days	02-09-21	03-09-21	₹ 0.00	₹ 0.00									
525		Manhole Cover	2 days	03-09-21	04-09-21	₹ 0.00	₹ 0.00									
526		Pipe Bridge	100 days	04-03-22	28-06-22	₹ 129,662.92	₹ 0.00									
527		Piling	26 days	04-03-22	02-04-22	₹ 2,199.01	₹ 0.00									
528		PCC	2 days	06-04-22	07-04-22	₹ 3,126.21	₹ 0.00									
529		Pier	15 days	20-04-22	06-05-22	₹ 71,733.92	₹ 0.00									
530		Pipe Bridge	26 days	25-05-22	23-06-22	₹ 51,961.33	₹ 0.00									
531		Laying of pipes	4 days	24-06-22	28-06-22	₹ 642.45	₹ 0.00									
532		Pump House	227 days	07-07-21	28-03-22	₹ 384,401.06	₹ 0.00									
533		Construction works	227 days	07-07-21	28-03-22	₹ 384,401.06	₹ 0.00									
534		Construction of pump house	32 days	07-07-21	12-08-21	₹ 88,443.12	₹ 0.00									
535		Footing	15 days	07-07-21	23-07-21	₹ 21,198.01	₹ 0.00									
536		Superstructure	7 days	24-07-21	31-07-21	₹ 37,463.92	₹ 0.00									
537		Rolling shutters, Wood works	10 days	02-08-21	12-08-21	₹ 20,032.54	₹ 0.00									
538		Plastering & Painting	10 days	02-08-21	12-08-21	₹ 9,748.66	₹ 0.00									
539		Compound Wall	180 days	31-08-21	28-03-22	₹ 295,957.93	₹ 0.00									
540		Footing	7 days	31-08-21	07-09-21	₹ 21,274.83	₹ 0.00									
541		Superstructure	15 days	11-09-21	28-09-21	₹ 37,458.69	₹ 0.00									
542		Plastering	4 days	29-09-21	02-10-21	₹ 72,821.74	₹ 0.00									
543		Structural steel work	4 days	24-03-22	28-03-22	₹ 164,402.67	₹ 0.00									
544		Road Works	242 days	20-09-21	28-06-22	₹ 25,641,319.18	₹ 0.00									
545		PWD Roads	26 days	20-09-21	19-10-21	₹ 5,836,137.00	₹ 0.00									
546		Excavation for Road work	7 days	20-09-21	27-09-21	₹ 290,369.41	₹ 0.00									
547		GSB	5 days	28-09-21	02-10-21	₹ 2,001,982.29	₹ 0.00									
548		WMM	5 days	04-10-21	08-10-21	₹ 1,876,438.87	₹ 0.00									
549		SS	4 days	09-10-21	13-10-21	₹ 68,224.45	₹ 0.00									
550		Bituminious Macadam	4 days	09-10-21	13-10-21	₹ 175,308.29	₹ 0.00									
551		RS	4 days	14-10-21	18-10-21	₹ 437,275.65	₹ 0.00									
552		BC	5 days	14-10-21	19-10-21	₹ 986,538.04	₹ 0.00									
553		LSGD Roads	21 days	20-10-21	12-11-21	₹ 6,439,755.80	₹ 0.00									
554		Berm Cutting	7 days	20-10-21	27-10-21	₹ 1,845,972.32	₹ 0.00									
555		Open graded premix carpet	5 days	28-10-21	02-11-21	₹ 126,038.30	₹ 0.00									
556		Concrete road surface	5 days	03-11-21	08-11-21	₹ 2,434,696.20	₹ 0.00									
557		Quarry Muck	4 days	09-11-21	12-11-21	₹ 2,033,048.98	₹ 0.00									

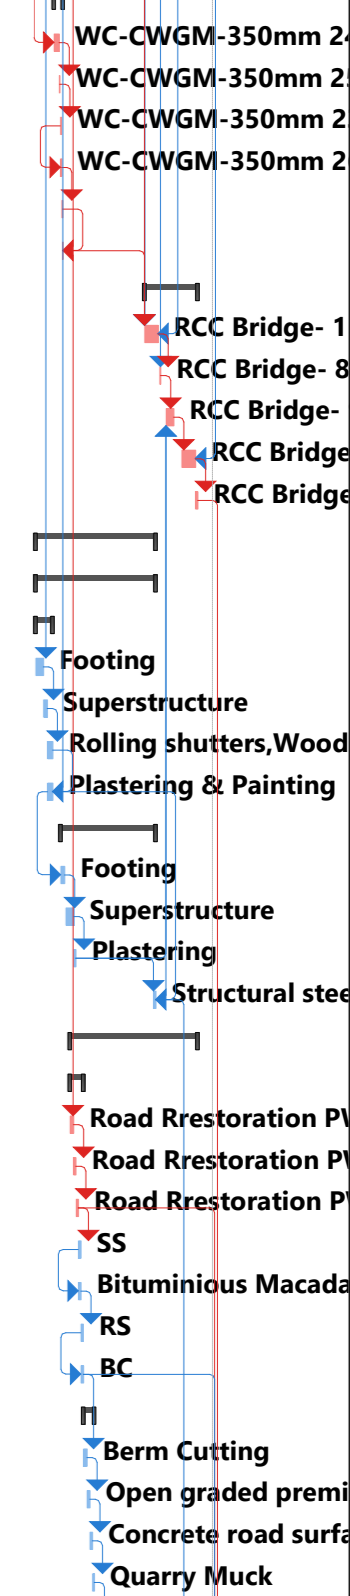

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	Cost	Payment Milestones - B1	2017	2018	2019	2020	2021	2022	2023
558		Pariyayam LSGD	12 days	13-11-21	26-11-21	₹ 7,576,958.48	₹ 0.00							
559		Open graded premix carpet	7 days	13-11-21	20-11-21	₹ 7,002,128.00	₹ 0.00							
560		Quarry Muck	5 days	22-11-21	26-11-21	₹ 574,830.48	₹ 0.00							
561		Common Jn	183 days	27-11-21	28-06-22	₹ 5,788,467.90	₹ 0.00							
562		Cutting	7 days	27-11-21	04-12-21	₹ 173,585.00	₹ 0.00							
563		Chipping	5 days	17-06-22	22-06-22	₹ 5,001,520.00	₹ 0.00							
564		Filling	5 days	23-06-22	28-06-22	₹ 613,362.90	₹ 0.00							
565		Trial run & Commissioning	26 days	30-05-22	28-06-22	₹ 0.00	₹ 0.00							
566		Project Finish	0 days	28-06-22	28-06-22	₹ 0.00	₹ 0.00							
567		Payment Milestones	529 days	20-11-20	30-07-22	₹ 0.00	₹ 162,063,923.08							
568		Payment Milestones 1	0 days	20-11-20	20-11-20	₹ 0.00	₹ 60,000,000.00							
569		Payment Milestones 2	0 days	31-12-20	31-12-20	₹ 0.00	₹ 16,800,000.00							
570		Payment Milestones 3	0 days	27-02-21	27-02-21	₹ 0.00	₹ 15,000,000.00							
571		Payment Milestones 4	0 days	30-04-21	30-04-21	₹ 0.00	₹ 14,000,000.00							
572		Payment Milestones 5	0 days	30-06-21	30-06-21	₹ 0.00	₹ 14,000,000.00							
573		Payment Milestones 6	0 days	31-08-21	31-08-21	₹ 0.00	₹ 6,000,000.00							
574		Payment Milestones 7	0 days	30-10-21	30-10-21	₹ 0.00	₹ 15,000,000.00							
575		Payment Milestones 8	0 days	31-12-21	31-12-21	₹ 0.00	₹ 7,000,000.00							
576		Payment Milestones 9	0 days	28-02-22	28-02-22	₹ 0.00	₹ 5,000,000.00							
577		Payment Milestones 10	0 days	30-04-22	30-04-22	₹ 0.00	₹ 3,000,000.00							
578		Payment Milestones 11	0 days	28-06-22	28-06-22	₹ 0.00	₹ 5,000,000.00							
579		Payment Milestones 12	0 days	30-07-22	30-07-22	₹ 0.00	₹ 1,263,923.08							

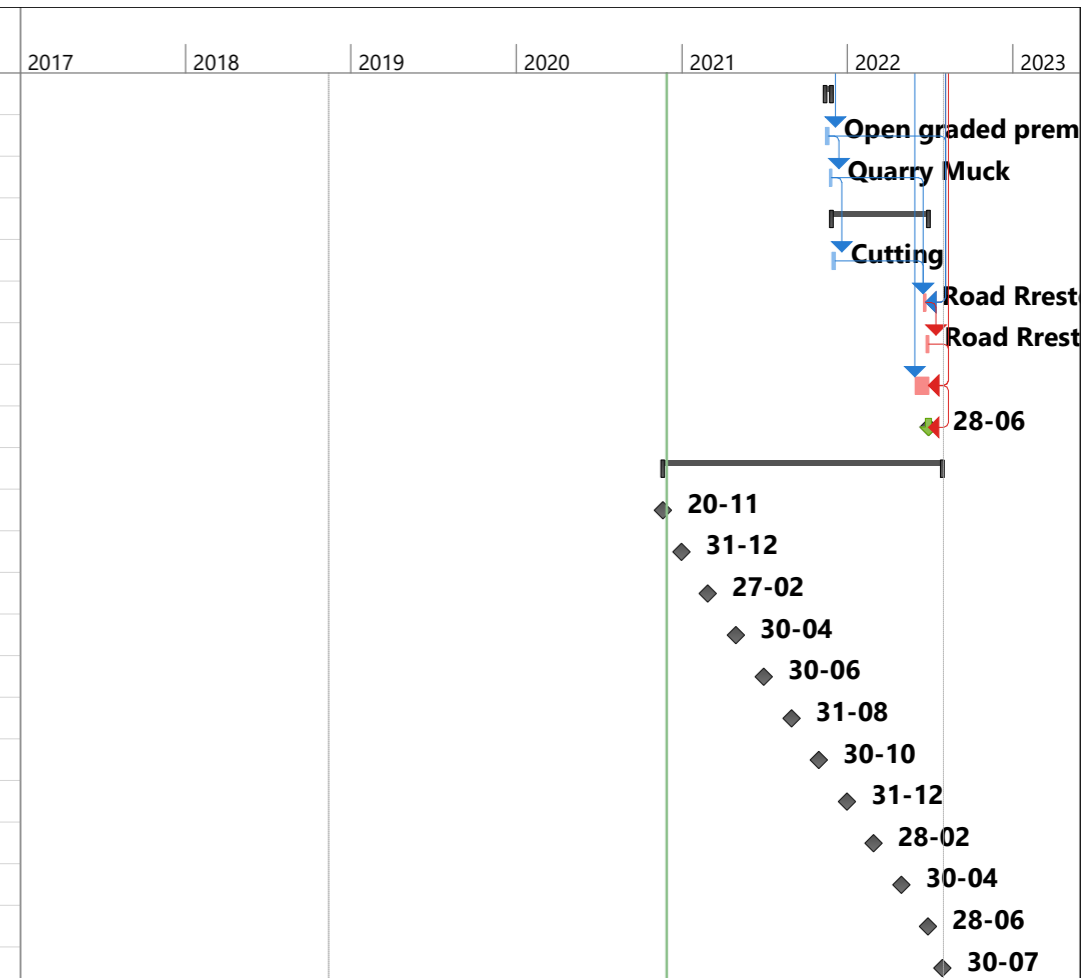

Project: WRD025-03-02-WSS to
Date: 28-11-20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
