


**Chengalloor Vattavila Work Schedule**

<b>Task</b>	<b>Start date</b>	<b>End date</b>	<b>Duration</b>
Project Execution	16-Oct-20	22-Mar-22	522
pit pits, levels marking for pipe lay	16-Oct-20	20-Oct-20	4
Dismantling bituminous road/Concrete/Inter locking paver block	21-Oct-20	31-Dec-20	71
Earth work in excavation for pipe laying	01-Jan-21	01-Apr-21	90
Close timbering for trenches/ Steel sheet shoring for pipe laying	02-May-21	31-Jul-21	90
Pipe laying, jointing, testing and back filling- PVC/SW	01-Aug-21	28-Aug-21	27
Earth work in excavation for MH	29-Aug-21	15-Sep-21	17
Close timbering for shafts/ Steel sheet shoring for MHs	16-Sep-21	03-Oct-21	17
Formwork for MHs - Shuttering and concrete	04-Oct-21	30-Nov-21	57
Steel reinforcement cutting & bending for MAT, Slab and steining, shuttering and concrete for MAT and Slab	01-Dec-21	27-Dec-21	26
Formwork and shuttering for steining	28-Dec-21	24-Jan-22	27
Steining concrete	25-Jan-22	10-Feb-22	16
Making connection (pipes to MHs)	11-Feb-22	21-Feb-22	10
PCC for joint blocks and channeling, PVC step fixing	22-Feb-22	28-Feb-22	6
Plastering of MHs	01-Mar-22	08-Mar-22	7
Conveying and fixing of cover slab & CI MH cover with frame	09-Mar-22	12-Mar-22	3
Back filling and removal of excess earth	13-Mar-22	21-Mar-22	8
Testing of system	22-Mar-22	22-Mar-22	0

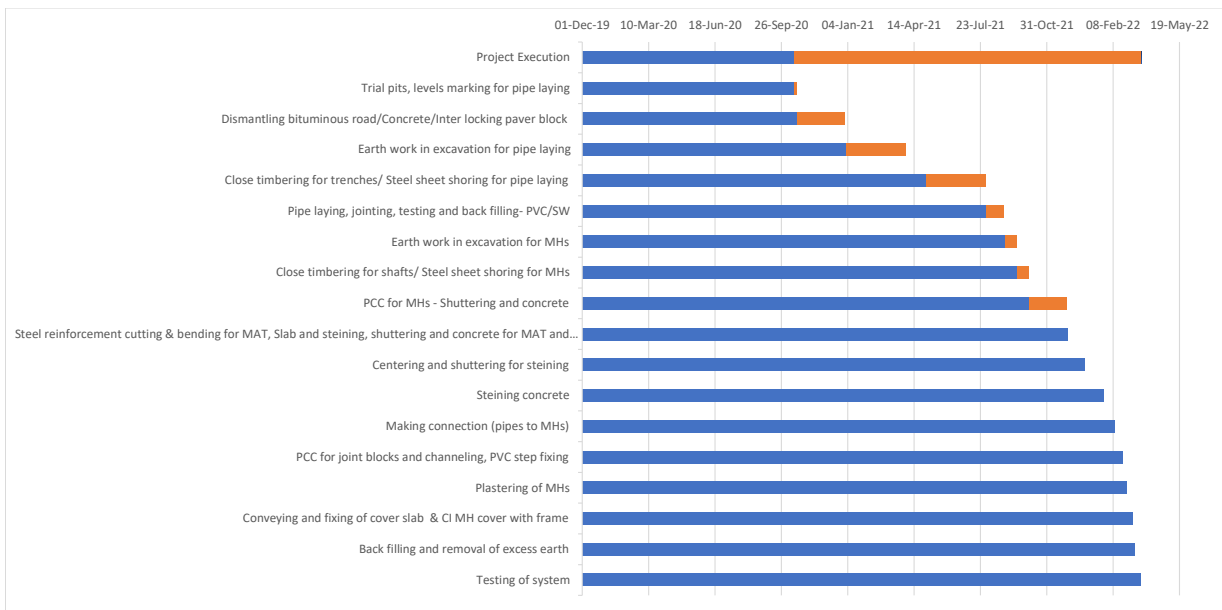

**Chengalloor Vattavila Implementation schedule**

<b>Jagathy Stilling Chamber</b>			
<b>Task</b>	<b>Start date</b>	<b>End date</b>	<b>Duration</b>
Project Execution	9-Oct-21	9-Oct-22	365
Dismantling bituminous road/Concrete/Inter locking paver block, Earth work in excavation for pipe laying	9-Oct-21	31-Aug-22	326
Close timbering for trenches/ Steel sheet shoring for pipe laying	9-Oct-21	31-Aug-22	326
Pipe laying, jointing with existing MH, testing and back filling- PVC/SW	9-Oct-21	31-Aug-22	326

