IMPLEMENTATION SCHEDULE

Construction of 13 LL OHSR at Edakochi

		June	Jul-21				Aug-21					Sep-21				Oct-21				Nov-21			
		24-30	1-7	8-14	15-21	22-28	29-4	5-11	12-18	19-25	26-1	2-8	9-15	16-22	23-29	30-6	7-13	14-20	21-27	28-3	4-10	11-17	18-24
1	10 Nos. Pile cap concreting																						
2	Ist stage columns - 17 Nos.																						
3	Ist stage columns - 18 Nos.																						
4	Ist Tie beam - 22 Nos																						
5	Ist Tie beam - 18 Nos																						
6	Ist Tie beam - 18 Nos																						
7	Iind stage columns - 17 Nos.																						
8	Iind stage columns - 18 Nos.																						
9	Iind Tie beam - 22 Nos																						
10	Iind Tie beam - 18 Nos																						
11	Iind Tie beam - 18 Nos																						
12	IIIrd stage columns - 17 Nos.																						
13	IIIrd stage columns - 18Nos.																						
14	Iiird Tie beam - 22 Nos																						
15	Iiird Tie beam - 18 Nos																						
16	Iiird Tie beam - 18 Nos																						
17	IVthstage columns - 17 Nos.																						
18	IVth stage columns - 18 Nos.																						
19	Supply of Pipes, valves and specials																						
20	Floor beam & slab shuttering work																						
21	Floor beam & slab reinforcement work																						
22	Floor beam & slab concreting																						
23	Side wall reinforcement work																						
24	side wall shuttering work																						
25	side wall concreting - Ist lift																						
26	side wall concreting - IInd lift																						
27	side wall concreting - IIIrd lift																						
28	Roof beam & slab shuttering work																						
29	Roof beam & slab reinforcement work																						
30	Roof beam & slab concreting																						
31	Plastering																						
32	Painting																						
33	Pipes and valves fixing																						
34	Landscaping																						

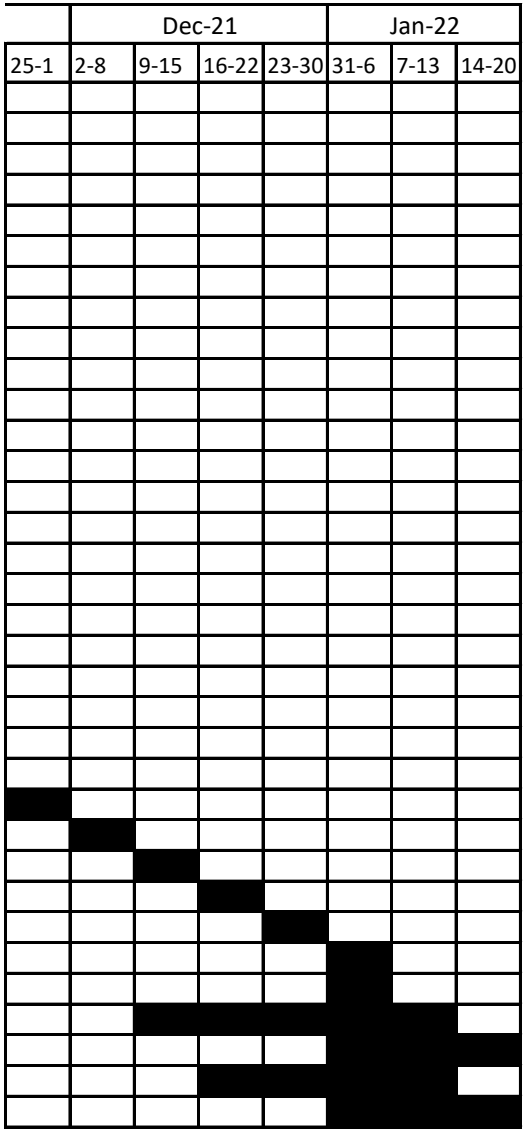
Dec-21
Jan-22
25-1
2-8
9-15
16-22
23-30
31-6
7-13
14-20
