Implementation plan - Sreenagar Manacaud

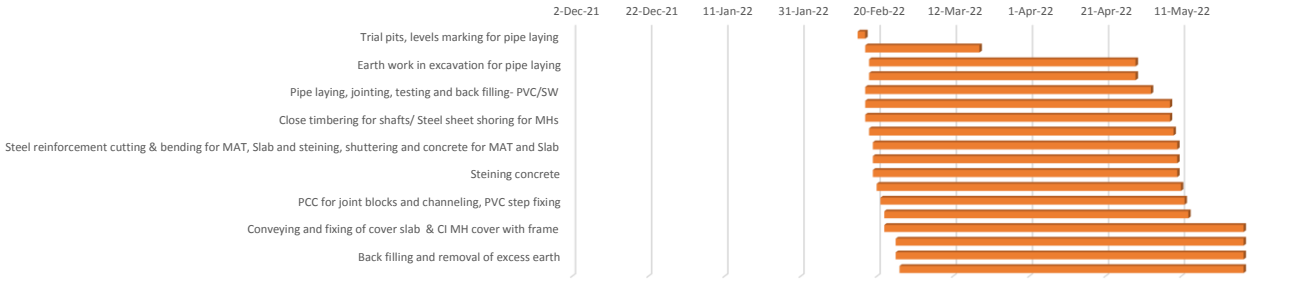

	Restoration of tar/cc/inter locking paver blocks	Back filling and removal of excess earth	Testing of system	Conveying and fixing of cover slab & CI MH cover with frame	Plastering of MHs	PCC for joint blocks and channeling, PVC step fixing	Making connection (pipes to MHs)	Steining concrete	Centering and shuttering for steining	Steel reinforcement cutting & bending for MAT, Slab and steining, shuttering and concrete for MAT and Slab	PCC for MHs - Shuttering and concrete	Close timbering for shafts/ Steel sheet shoring for MHs	Earth work in excavation for MHs	Pipe laying, jointing, testing and back filling- PVC/SW	Close timbering for trenches/ Steel sheet shoring for pipe laying	Earth work in excavation for pipe laying	Dismantling bituminous road/Concrete/Inter locking paver block	Trial pits, levels marking for pipe laying
Start date	26-Feb-22	25-Feb-22	25-Feb-22	22-Feb-22	22-Feb-22	21-Feb-22	20-Feb-22	19-Feb-22	19-Feb-22	19-Feb-22	18-Feb-22	17-Feb-22	17-Feb-22	17-Feb-22	18-Feb-22	18-Feb-22	17-Feb-22	15-Feb-22
Days to complete	95	95	95	95	80	80	80	80	80	80	80	80	80	75	70	70	30	2
