Implementation plan - Central Theatre

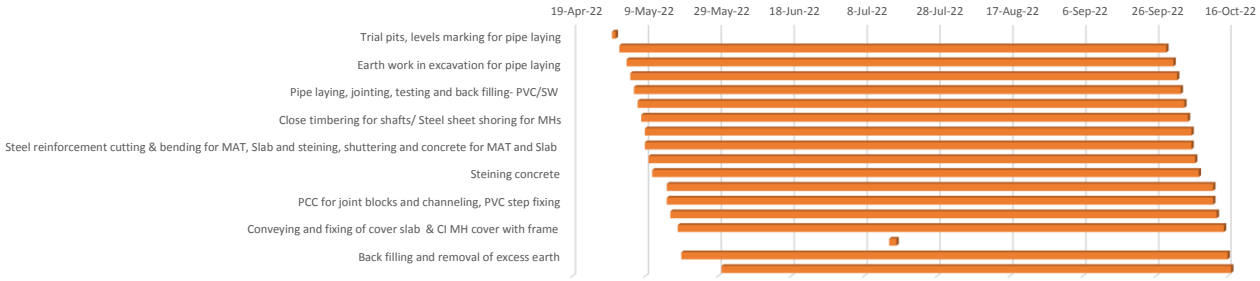

	Restoration of tar/cc/inter locking paver blocks	Back filling and removal of excess earth	Testing of system	Conveying and fixing of cover slab & CI MH cover with frame	Plastering of MHs	PCC for joint blocks and channeling, PVC step fixing	Making connection (pipes to MHs)	Steining concrete	Centering and shuttering for steining	Steel reinforcement cutting & bending for MAT, Slab and steining, shuttering and concrete for MAT and Slab	PCC for MHs - Shuttering and concrete	Close timbering for shafts/ Steel sheet shoring for MHs	Earth work in excavation for MHs	Pipe laying, jointing, testing and back filling- PVC/SW	Close timbering for trenches/ Steel sheet shoring for pipe laying	Earth work in excavation for pipe laying	Dismantling bituminous road/Concrete/Inter locking paver block	Trial pits, levels marking for pipe laying
Start date	30-May-22	19-May-22	15-Jul-22	18-May-22	16-May-22	15-May-22	15-May-22	11-May-22	10-May-22	9-May-22	9-May-22	8-May-22	7-May-22	6-May-22	5-May-22	4-May-22	2-May-22	30-Apr-22
Days to complete	140	150	2	150	150	150	150	150	150	150	150	150	150	150	150	150	150	1
