

Phone: 0491-2544927  
phcirclepkd@gmail.com



## KERALA WATER AUTHORITY

Office of the Superintending Engineer,  
P.H. Circle, Kalmandapam, Palakkad.

No. KWA/PHC/PKD/JJM/Karakurussi/21-22

Date : 20.02.2023

From

Superintending Engineer

To

The Executive Engineer  
W.S.P Division,  
Kerala Water Authority,  
Palakkad

Sir,

Sub: JAL JEEVAN MISSION- 2020-21- WSS to Karakurissi panchayath supplying, laying, testing, commissioning and maintenance of distribution systems with providing FHTCs - 2623 Nos in Karakurissi Panchayath - 1<sup>st</sup> supplemental agreement for time extension and time extension proceedings- forwarding - Reg.

Ref :- Agrt No. 01/22-23/SE/PHC/PKD dated 07.04.2022


I am forwarding herewith the 1<sup>st</sup> Supplemental agreement for time extension and time extension proceedings of the subject work for further necessary action.

Yours faithfully,

Superintending Engineer

*K. T. S.* ✓

Encl : 1st Supplemental agreement for time extension and proceedings.

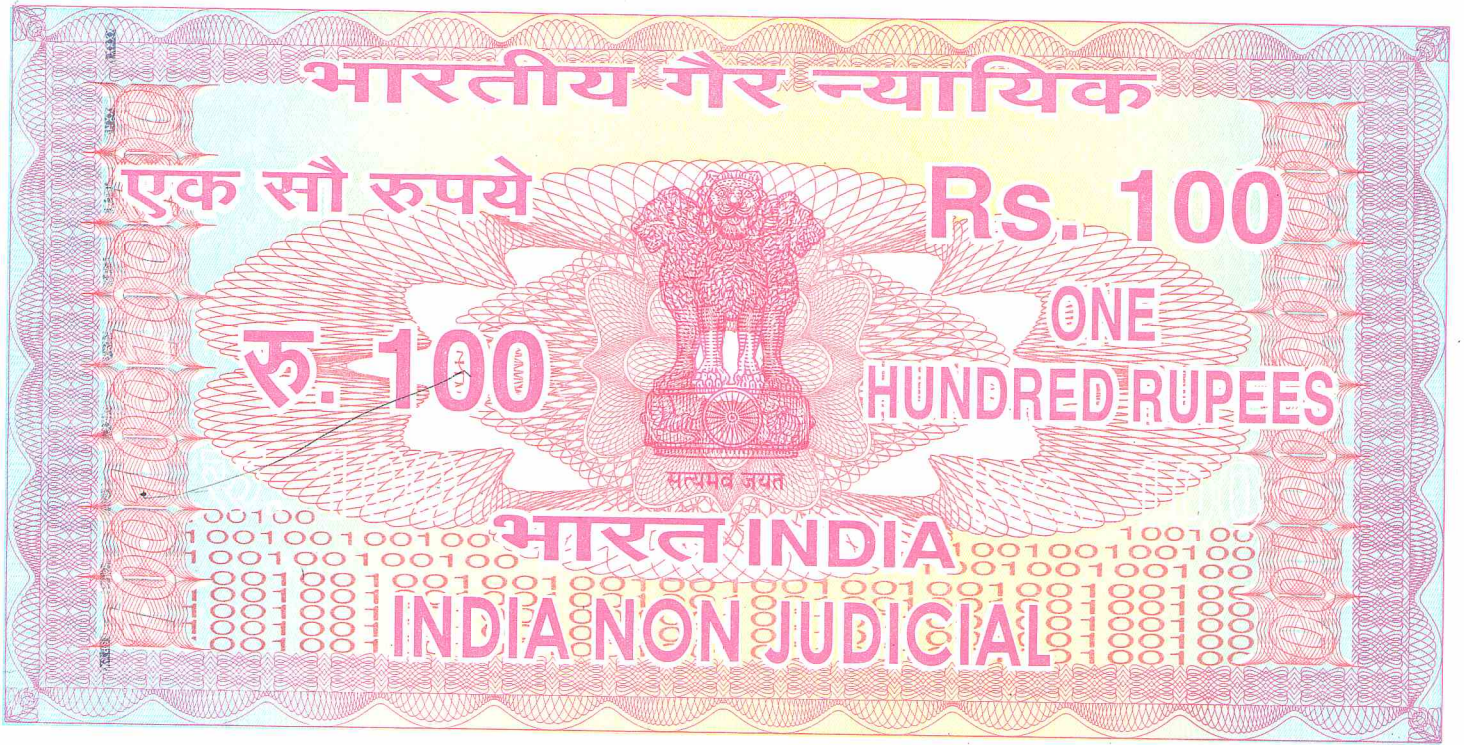

കേരളം കേരल KERALA

DH 576884

**1<sup>st</sup> Supplemental Agreement to Agreement No. 01/22-23/SE/PHC/PKD  
FOR 1<sup>st</sup> EXTENSION OF TIME**

THIS SUPPLEMENTAL AGREEMENT executed on this the 10<sup>th</sup> day of February Two Thousand Twenty Three (2023) by Sri K.I Paulose , Kunnel House, Kinnackal (PO), Muvattupuzha (hereinafter referred to as the contractor which expression shall include his heirs, executors, administrators and permitted assigns) in favour of the Kerala Water Authority (hereinafter referred to as "The Authority").

WHEREAS the contractor has executed an agreement bearing No. 01/22-23/SE/PHC/PKD dt. 07.04.2022 (Hereinafter referred to as the Principal agreement) for the work of "JAL JEEVAN MISSION- 2020-21- WSS to Karakurissi panchayath supplying, laying, testing, commissioning and maintenance of distribution systems with providing FHTCs – 2623 Nos in Karakurissi Panchayath " with the Authority and has agreed to complete the said work on or before 29.12.2022 in accordance with the said agreement.

Contractor

Superintending Engineer

42196 100 07/2/22

MUVATTUPUZHA VENDOR  
K.A GOPALAN

K.I.PAULOSE  
Govt. A' Class Contractor of  
PWD & KWA  
Kunnel House, Kinnackal P.O.  
Muvattupuzha, Ernakulam - 682 316





കേരളം കേരल KERALA

DH 576883

WHEREAS the contractor could not complete the work within period specified in the Principal agreement.

WHEREAS the contractor has submitted an application requesting for extension of time of completion originally agreed to for a period up to 30.06.2023 by stating that the statutory permission for laying pipe along PWD road is still pending which delayed the work and the Executive Engineer, WSP Division, Palakkad has recommended for granting time extension upto 31.05.2023 without imposing fine. The Authority has agreed to the said request & recommendation and issued a proceedings No. KWA/PHC/PKD/JJM/ Karakurissi / 21-22 dated: 10.02.2023 for granting time extension up to 31.05.2023 without imposing fine.

AND WHEREAS the Authority have agreed to allow extending of time for the completion of the said work subject to the terms and conditions hereinafter appearing.

The period of time for completion of the work under the Principal agreement is extended up to 31.05.2023 from 29.12.2022 without imposing fine.

Contractor

Superintending Engineer

No. 42195 RS 100 03/02/22

Sold to.....  
MOOVATTUPUZHA VENDOR  
K.A GOPAKUMAR

K.I.PAULOSE  
Govt. A' Class Contractor of  
PWD & KWA  
Kunneel House, Punnackal P.O.  
Muvattupuzha, Ernakulam - 682 316  
(3)




The contractor shall carry out all further works as under the Principal agreement within the said extended period at the rates and in the manner agreed to therein subject to all the other conditions prescribed in the said agreement and shall not claim any enhanced rate for each items of work on account of the extension of time, either due to the increase in rates of labour or materials or on any other ground whatsoever.

As modified above, the Principal deed shall be and remain in full force and effect.


In witness Sri K.I Paulose , Kunnel House, Kinnackal (PO), Muvattupuzha. The contractor has hereunto set their hands the day, month and year first above written.

Signed by Sri K.I Paulose , Kunnel House, Kinnackal (PO), Muvattupuzha



CONTRACTOR

In the presence of:-

1. R. Pradeep  
D/merit, KWA, PHC, PKD
2. Abdul Fahad A   
UP TYPIS, KWA, PHC, PKD



SUPERINTENDING ENGINEER
